



Golden State
Water Company
A Subsidiary of American States Water Company

February 1, 2017

***VIA ELECTRONIC FILING AND
OVERNIGHT DELIVERY***

Mr. Timothy Sullivan
Executive Director
California Public Utilities Commission
505 Van Ness Avenue
San Francisco, CA 94102-3298

**RE: Bear Valley Electric Service (U 913 E) Second Annual Report on the Mobile Home
Park Utility Update Program**

In accordance with California Public Utilities Commission Decision 14-03-021, Section 4.3.4, and ordering paragraphs 10 and 11, Golden Water Company on behalf of its division Bear Valley Electric Service (BVES) submits its second annual report on the program to convert master-metered mobile home parks (MHP) to direct utility service.

It is respectfully requested that all formal correspondence and Staff requests regarding this filing be addressed to the following:

By Email: nquan@gswater.com

By regular mail: Nguyen Quan
Golden State Water Company
630 E. Foothill Blvd
San Dimas, CA 91773

Informal inquiries may be directed to Ronald Moore at (909) 394-3600.

Sincerely,

Nguyen Quan
Manager, Regulatory Affairs

Enclosure

cc: President Michael Picker

Commissioner Carla J. Peterman
Commissioner Liane M. Randolph
Commissioner Martha Guzman Aceves
Commissioner Clifford Rechtschaffen
Chief ALJ Karen Clopton
Edward Randolph, Director, Energy Division
Elizaveta Malashenko, Director, SED
Sunil Shori, Safety Enforcement Division



Bear Valley
Electric Service
A Division of Golden State Water Company

BEAR VALLEY ELECTRIC SERVICE (U913 E)

MOBILE HOME PARK UTILITY UPGRADE PROGRAM SECOND ANNUAL STATUS REPORT

In Compliance with:
Decision 14-03-021

Reporting Period:
January 1, 2016 through December 31, 2016

February 1, 2017

TABLE OF CONTENTS

I. Introduction.....	2
II. Implementation Timeline	3
III. Program Status.....	4
IV. Conclusion.....	4

**BEAR VALLEY ELECTRIC SERVICE (U913 E)
MOBILE HOME PARK UTILITY UPGRADE PROGRAM
SECOND ANNUAL STATUS REPORT**

I. Introduction

On March 14, 2014, the California Public Utilities Commission (Commission) issued Decision (D). 14-03-021, and authorized the establishment of the Mobilehome Park Utility Upgrade Program (MHP Program). The MHP Program is a voluntary three year pilot program with the goal of converting approximately 10 percent of the Mobilehome Parks (MHP) spaces within each of the Commission regulated energy utilities' service territories.

Bear Valley Electric Service (BVES) serves 7 master-metered sub-metered MHPs. Of these 7 MHPs, 3 applied for the MHP Program and one was prioritized by the Commission Safety and Enforcement Division (SED). There are approximately 63 spaces prioritized for conversion.


In D.14-03-021, the Commission requires annual reports be prepared to confirm the utilities progress in implementing the pilot program. Reports are due by February 1 in the year following each of the three calendar years of the MHP Program. Pursuant to D.14-03-021, Ordering Paragraph 10 (b) states as follows:

“By February 1, 2017, a status report that identifies timeline status and preliminary quantification of construction costs incurred per space, broken out on both “to the meter” and “beyond the meter” bases, as further described in the body of this Order.”

BVES submits its Second Annual Status Report for the period January 1, 2016 through December 31, 2016.

II. Implementation Timeline

Bear Valley Electric Services' implementation timeline for one prioritized MHP is reflected below:

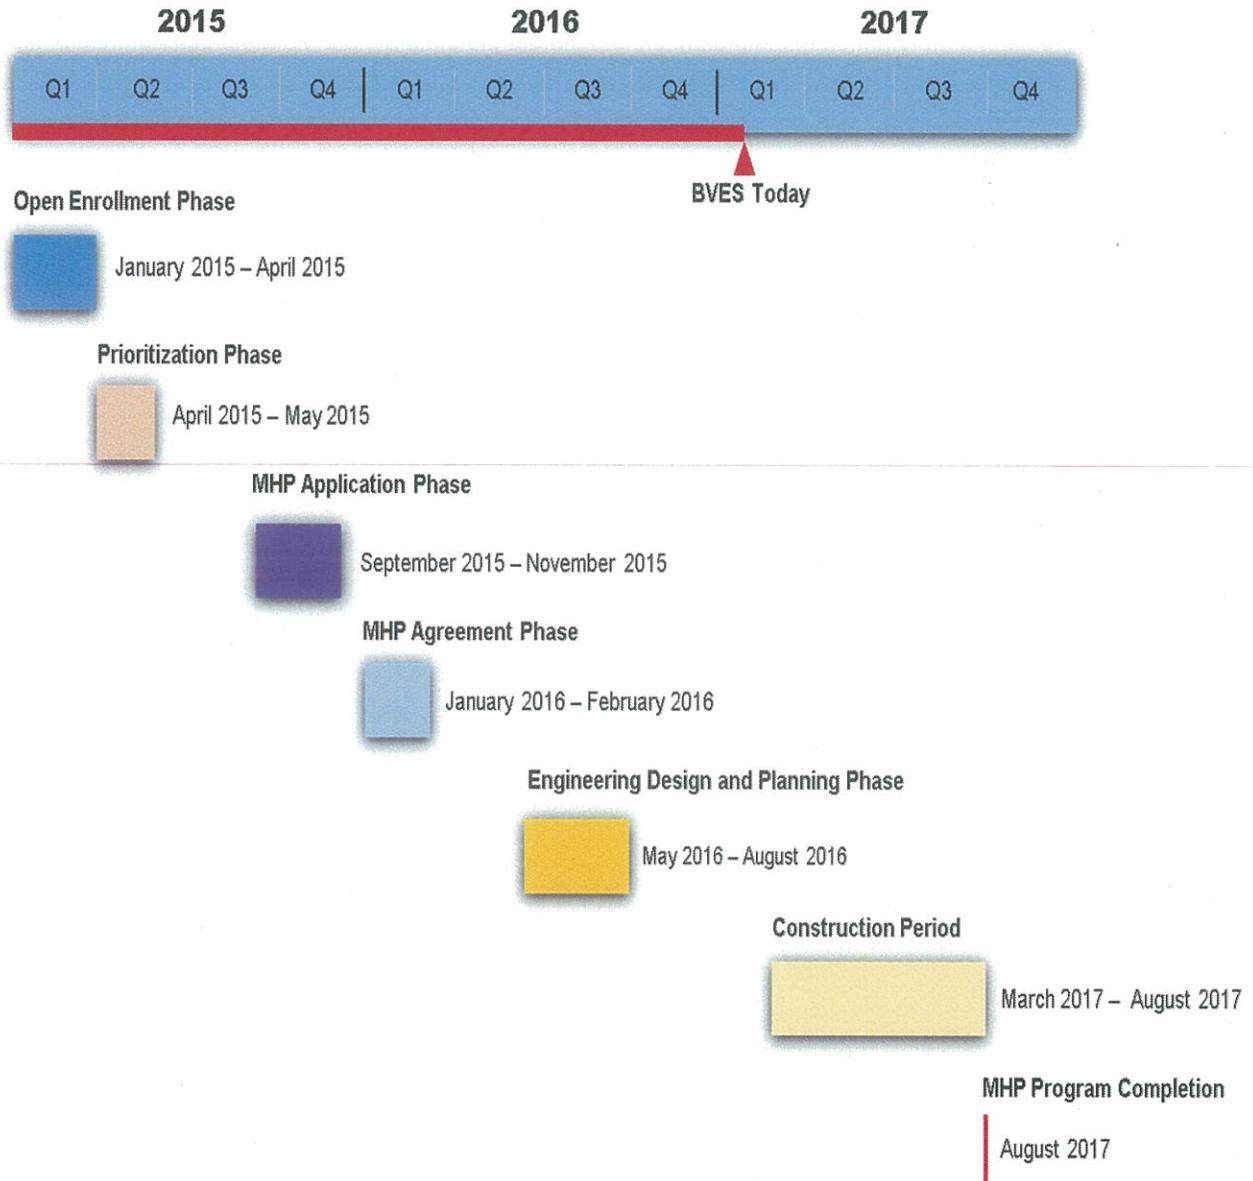

III. Program Status

In February 2016 BVES signed, with representatives of the prioritized MHP, the agreement to participate in the MHP Program. In May 2016 BVES started the Engineering Design and Planning Phase. The engineering design is to connect BVES' system "to the meter" of each of the MHP coaches. This phase was completed in August 2016.

Following the completion of the Engineering Design and Planning Phase, BVES informed the MHP representatives that, pursuant to the MHP Program agreement it is their responsibility to find contractors to perform the "beyond the meter" phase. A contractor was retained by the MHP.

BVES plans to begin the construction phase in March 2017 and it anticipates to complete this phase by August 2017. The MHP Program is currently on hold until the end of February 2017 due to extreme winter weather conditions in BVES' service territory.

IV. Conclusion

BVES is committed to implement a successful MHP Program with its prioritized MHP. BVES will provide the Commission with additional updates and status reports as needed.

Certification

I have reviewed, or have caused to be reviewed, this compliance submittal.


Based on my knowledge, information, or belief, this compliance submittal does not contain any untrue statement of a material fact or omit to state a material fact necessary to make the statements true.

Based on my knowledge, information, or belief, this compliance submittal contains all of the information required to be provided by Commission Orders, rules and regulations.

I declare under penalty of perjury that the foregoing is true and correct.

Executed on February 1, 2017, at San Dimas, California.

GOLDEN STATE WATER COMPANY



Keith Switzer
Vice President, Regulatory Affairs
(909) 394-3600 ext. 759
kswitzer@gswater.com
